

ID	Task Name	Duration	Start	Finish	Predecessors	Jan 14, '07						
						T	W	T	F	S	S	M
1	Single Family House - Architect Design (3,000 square feet)	99 days?	Thu 1/11/07	Tue 5/29/07		[Project Summary Bar]						
2	General Conditions	2 days	Thu 1/11/07	Fri 1/12/07		[External Milestone Bar]						
3	Finalize plans and develop estimate with owner, arct	0 days	Thu 1/11/07	Thu 1/11/07		[Milestone 1/11]						
4	Sign contract and notice to proceed	0 days	Thu 1/11/07	Thu 1/11/07	3	[Milestone 1/11]						
5	Apply for Permits	2 days	Thu 1/11/07	Fri 1/12/07		[External Milestone Bar]						
6	Secure foundation permit	0 days	Thu 1/11/07	Thu 1/11/07	4	[Milestone 1/11]						
7	Secure framing permit	0 days	Thu 1/11/07	Thu 1/11/07	4	[Milestone 1/11]						
8	Secure electrical permit	0 days	Thu 1/11/07	Thu 1/11/07	4	[Milestone 1/11]						
9	Secure plumbing permit	2 days	Thu 1/11/07	Fri 1/12/07	4	[Task: General contractor]						
10	Secure HVAC permit	0 days	Thu 1/11/07	Thu 1/11/07	4	[Milestone 1/11]						
11	Secure miscellaneous permits	0 days	Thu 1/11/07	Thu 1/11/07	4	[Milestone 1/11]						
12	Site Work	3 days	Mon 1/15/07	Wed 1/17/07		[External Milestone Bar]						
13	Clear and grub lot	1 day	Mon 1/15/07	Mon 1/15/07	6,7,8,9,11,10	[Task: Site excavation co]						
14	Install temporary power service	1 day	Tue 1/16/07	Tue 1/16/07	13	[Task: Electric compa]						
15	Install underground utilities	1 day	Wed 1/17/07	Wed 1/17/07	14	[Task: Electric co]						
16	Foundation	39 days?	Thu 1/11/07	Tue 3/6/07		[Project Summary Bar]						
17	Excavate for foundations	13 days	Thu 1/18/07	Mon 2/5/07	15	[Task]						
18	Perform foundation inspection	1 day	Tue 3/6/07	Tue 3/6/07	23,17	[Task]						
19	Form basement walls	4 days	Tue 2/6/07	Fri 2/9/07	17	[Task]						
20	Place concrete for foundations & basement walls	5 days	Mon 2/12/07	Fri 2/16/07	19	[Task]						
21	Cure basement walls for 7 days	7 days	Mon 2/19/07	Tue 2/27/07	20	[Task]						
22	Strip basement wall forms	2 days	Wed 2/28/07	Thu 3/1/07	21	[Task]						
23	Waterproof/insulate basement walls	2 days	Fri 3/2/07	Mon 3/5/07	22	[Task]						
24	Backfill foundation	2 days	Thu 1/11/07	Fri 1/12/07		[Task: Site excavation contractor]						
25	Deliver lumber	1 day?	Mon 1/15/07	Mon 1/15/07	24	[Task]						
26	Deliver steel	1 day?	Tue 1/16/07	Tue 1/16/07	25	[Task]						
27	Framing	26 days?	Wed 1/17/07	Wed 2/21/07		[External Milestone Bar]						
28	Install 1st floor joists	2 days	Wed 1/17/07	Thu 1/18/07	26	[Task: Frami]						
29	Lay 1st floor decking	1 day	Fri 1/19/07	Fri 1/19/07	28	[Task: Fr]						
30	Frame 1st floor walls	3 days	Mon 1/22/07	Wed 1/24/07	29	[Task]						
31	interior walls	2 days	Thu 1/25/07	Fri 1/26/07	30	[Task]						
32	Install 2nd floor joists	2 days	Mon 1/29/07	Tue 1/30/07	31	[Task]						


Project: Residential Construction
Date: Mon 6/2/08

Task [Patterned Box]
Split [Dotted Line]
Progress [Solid Black Bar]

Milestone [Diamond]
Summary [Thick Black Bar]
Project Summary [Thick Grey Bar]

External Tasks [Light Purple Box]
External Milestone [Diamond]
Deadline [Green Arrow]

ID	Task Name	Duration	Start	Finish	Predecessors	7 Jan 14, '07													
						T	W	T	F	S	S	M	T	W	T	F	S		
33	Frame 2nd floor decking	2 days	Wed 1/31/07	Thu 2/1/07	32														
34	Deliver trusses	1 day?	Fri 2/2/07	Fri 2/2/07	33														
35	Frame 2nd floor walls	3 days	Mon 2/5/07	Wed 2/7/07	34														
36	interior walls	3 days	Thu 2/8/07	Mon 2/12/07	35														
37	build trusses	1 day?	Tue 2/13/07	Tue 2/13/07	36														
38	set trusses	1 day?	Wed 2/14/07	Wed 2/14/07	37														
39	Complete roof framing	3 days	Thu 2/15/07	Mon 2/19/07	38														
40	finish interior framing	2 days	Tue 2/20/07	Wed 2/21/07	39														
41	Dry In	72 days?	Thu 1/11/07	Fri 4/20/07															
42	stock roofing	1 day	Thu 2/22/07	Thu 2/22/07	40														
43	Install felt, flashing and shingles	3 days	Wed 4/18/07	Fri 4/20/07	55,42														
44	Deliver exterior doors	1 day?	Thu 1/11/07	Thu 1/11/07															
45	Deliver windows	1 day?	Thu 1/11/07	Thu 1/11/07															
46	Hang 1st floor exterior doors	1 day	Thu 1/11/07	Thu 1/11/07															
47	Install 1st floor windows	1 day	Thu 1/11/07	Thu 1/11/07															
48	Install 2nd floor windows	1 day	Thu 1/11/07	Thu 1/11/07															
49	Exterior Finishes	19 days	Thu 1/11/07	Tue 2/6/07															
50	Complete exterior siding	15 days	Thu 1/11/07	Wed 1/31/07															
51	install columns,rails,shutters	3 days	Fri 2/23/07	Tue 2/27/07	42														
52	install stone work	8 days	Fri 1/12/07	Tue 1/23/07	48														
53	scrape out	1 day	Tue 2/20/07	Tue 2/20/07	39														
54	Utility Rough-Ins and Complete Concrete	72 days?	Thu 1/11/07	Fri 4/20/07															
55	ground rough in	3 days	Fri 4/13/07	Tue 4/17/07	51,81														
56	ground rough inspection	1 day	Wed 4/18/07	Wed 4/18/07	55														
57	Place concrete for basement floor	2 days	Thu 4/19/07	Fri 4/20/07	56														
58	Install firebox install	1 day?	Thu 1/11/07	Thu 1/11/07															
59	Rough-in HVAC	3 days	Tue 3/13/07	Thu 3/15/07	63,60														
60	Rough-in electrical	5 days	Wed 2/28/07	Tue 3/6/07	53,51														
61	Install vac system	1 day?	Wed 3/7/07	Wed 3/7/07	60														
62	Rough-in communication - phone, cable, computer, :	2 days	Thu 3/8/07	Fri 3/9/07	53,61														
63	total rough inspection	1 day	Mon 3/12/07	Mon 3/12/07	62														
64	complete inspection deficiencies	1 day	Fri 3/16/07	Fri 3/16/07	59														

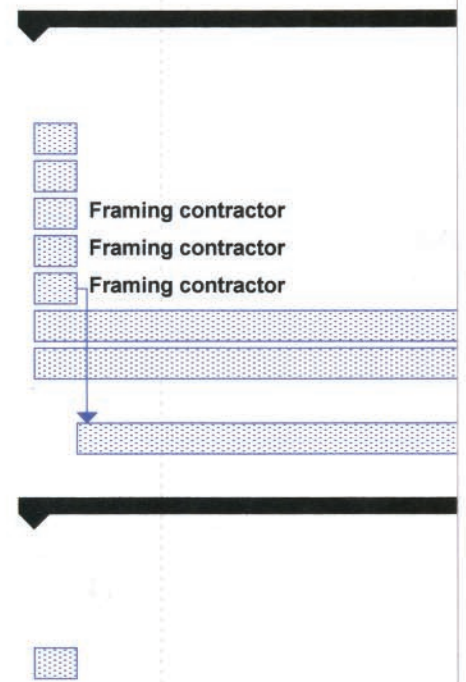

Project: Residential Construction Date: Mon 6/2/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
